
Measure DD (2002), the Oakland Trust for Clean Water and Safe Parks

Project update July 17, 2023



No updates

- 1. Glen Echo Creek Restoration last update March 2023
- 2. Creek Restoration of Beaconsfield Branch Sausal Creek last update May 2022
- 3. Measure DD Coalition Administrative Support Contract implementation underway
- 4. EBRPD Waterfront Trail Sites

1.Crowley Site

2.Gallagher & Burk (344 High Street – Oliver De Silva Inc., owner)

3.Hanson Aggregates (4501 Tidewater Avenue) – Home Dock Properties

Tide Gate Operations Manual for the 7th Street Flood Control Facility

- As of 7/17/23, the City is waiting for final comments on the memo from the District.
- City Watershed staff met with District staff on 7/6/23. The District is still planning to provide written comments on the manual so the City can finalize it. The manual will not be used by the District at this time, but once finalized it will provide general information on tide gate operations.
- Comments from the Measure DD Coalition on the memo have been shared with the District.

Decomposed Granite Path Around Lake Merritt

- Project manager is continuing to work on securing a contract to complete the work.
- A quote from a subcontractor was received and is being evaluated by the City. After the contract is negotiated and executed, the City will provide an estimated completion date for the project.

Lake Merritt Interpretive Signs




www.oaklandca.gov/topics/lake-merritt-interpretive-signs

Lake Merritt Interpretive Signs

- Installed week of May 15, 2023
- View signs at webpage below



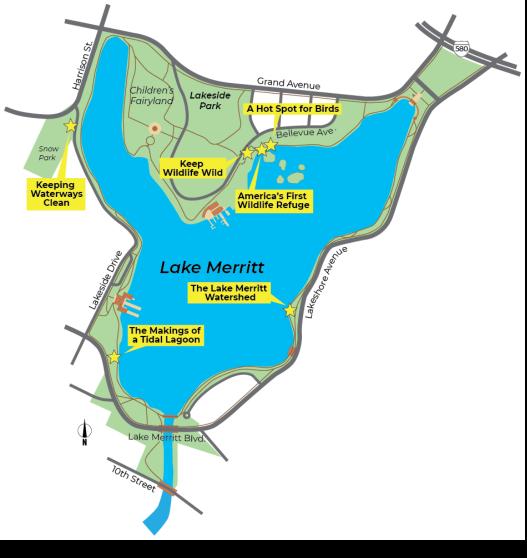

www.oaklandca.gov/topics/lake-merritt-interpretive-signs

Lake Merritt Channel Improvements at 10th Street






Lake Merritt Channel at 10th Street

Challenges

- SF Regional Water Quality Control Board (Water Board) responded to proposed re-planting plan needed to close out regulatory permits
- 2. New Water Board policy: monitor & report for 10 years post-installation of replacement trees, and 5 years for shrubs and other plantings - overall 80% survival rate.
- 3. Funding is not available for more that 2 or 3 years of post-project monitoring.
- Homeless encampments present outside fenced-off wetland area. Project Manager will need to work with the Encampment Management Team (EMT) prior to construction. The status of encampments at the site were documented 7/16/23 and will be reported to the EMT.



Oakland Waterfront Access, Parks, and Cleanup

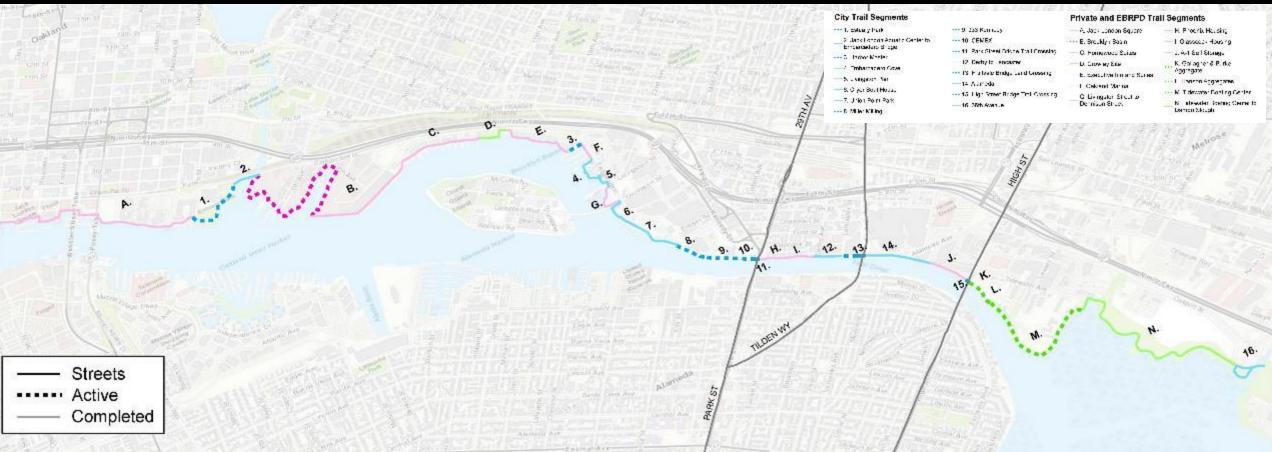

https://cao-94612.s3.amazonaws.com/documents/Info-Memo-Waterfront-Trails-Update.pdf

Fruitvale Land Crossing Bay Trail Segment

- Project to complete the Fruitvale Land Crossing Bay Trail segment (approximately 420 linear feet).
- Construction has begun and is anticipated to continue through November 2023.

Estuary Park

- Project awarded CA Coastal Conservancy Climate Adaptation fund grant for enhanced design of the living shoreline. Draft California Environmental Quality Act Environmental Impact Report Addendum and 95% Documentation paused to allow time for the enhanced shoreline design to advance/catch up. Technical work on this project is continuing.
- Also, planning for funding project construction with Series D Measure DD funds: See <u>Parks & Open Spaces</u> (opengov.com)

www.oaklandca.gov/projects/estuary-park



Union Point Park to 23rd Avenue Trail aka Miller Milling to Cemex E. 7th St to 23rd/29th Aves

- Draft of Phase II Environmental Site Assessment Report complete and under revision.
- Order-of-magnitude cost estimates for easement acquisitions of the three private properties received from consultant – under review.
- Geotech report under review
- Project and Grant Management Division staffing changes



Creek and Waterway Restoration



Courtland Creek Restoration



Creek restoration

- Construction contract executed June 8, 2023, NTP June 18
- Construction underway
- Completion expected spring 2024

Acquisitions

- Consultant provided list of top 200 parcels to consider based on ecological and equity parameters
- 2. Staff to evaluate for feasibility and make recommendation on a subset of parcels to pursue

